


PARKS UPDATE OFFICE OF CAPITAL IMPROVEMENTS JULY 19, 2023



Parks GO Bond and Yacht Club

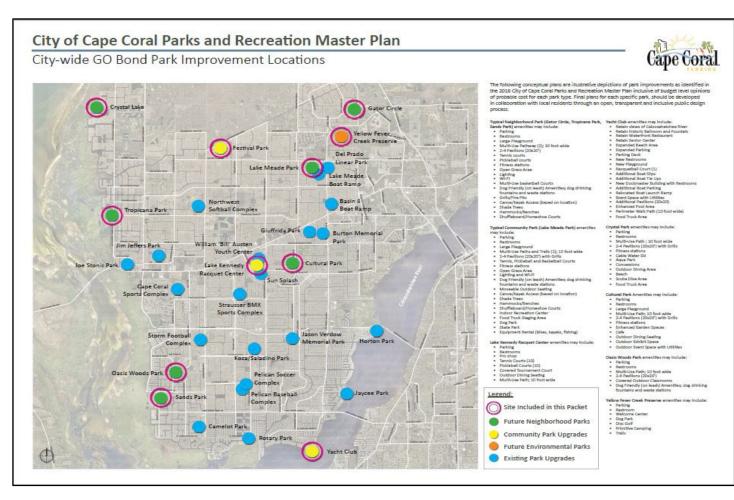

- 1. Giuffrida Park Open
- 2. Del Prado Linear Park Open
- 3. Gator Trails Park Open Add. Scope
- 4. Cultural Park Open Add. Scope
- 5. Sands Soft Opening Sub. Complete - Additional Scope
- 6. Coviello Construction 95% Complete
- 7. Yellow Fever Const. 40% Complete
- 8. Lake Kennedy Const. 25% Complete
- 9. Crystal Lake Proposed Bidding in July
- 10. Festival Park Prop. Bidding in August
- 11. Lake Meade Prop. Bidding in August
- 12. Tropicana Permitting
- 13. Yacht Club Permitting



Gator Trails Park - Open



Contractor: Waypoint Contracting, Inc.

Original Contract Scope

- Contract Amount: \$2,114,588
- 5% Contingency: <u>\$ 105,729*</u>
- Budget: \$2,220,317
- *Contingency used for Cultural or Gator Trails
- Original Schedule: Substantially Complete
- Original Budget: Under Budget



Gator Trails Park - Open



Contractor: Waypoint Contracting, Inc.

Additional Scope In Process:

- 1. Replace trees damaged by Hurricane Ian.
- 2. Add shade over existing benches.
- 3. Add shade over existing exercise equipment.
- 4. Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Cultural Park - Open



Contractor: Waypoint Contracting, Inc.

Original Contract Scope

- Contract Amount: \$2,938,141
- 5% Contingency: <u>\$ 146,907*</u>
- Budget: \$3,085,048
- * Contingency used for Cultural or Gator Trails
- Original Schedule: Substantially Complete
- Original Budget: Under Budget



Cultural Park - Open



Contractor: Waypoint Contracting, Inc.

Additional Scope In Process:

- 1. Install perimeter sidewalks Completed.
- 2. Added 60 new trees and vegetation (Arbor Day Foundation Grant) Completed.
- 3. Replace trees damaged by Hurricane Ian. Adding 30 trees.
- 4. Add shade over existing benches.
- 5. Add exercise equipment with shade.
- 6. Curb and Landscape 3 medians.
- 7. Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Sands Park - Soft Opening



- Contract Amount: \$3,188,751
- 5% Contingency:
- Budget:

<u>\$ 159,438*</u> \$3,348,189

*Contingency used for Sands or Coviello

Substantial Completion - April 2023

 Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Contractor: Wright Construction

Joe Coviello Park



- Contract Amount: \$ 1,996,981
- 5% Contingency: <u>\$ 99,849*</u>
- Budget:

\$ 2,096,830

*Contingency used for Sands or Coviello Parks

- Prop. Substantial Completion Aug 2023
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Contractor: Wright Construction

Yellow Fever Creek





Contractor: OAC Action Construction

- Contract Amount: \$5,739,321
- 5% Contingency: <u>\$ 286,966</u>
- Budget:

- \$6,026,287
- Construction is 40% complete
- Schedule: Completion November 2023
- Budget: On Budget
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat

Lake Kennedy Racquet Center




Contractor: Charles Perry Partners, Inc.

- **Contract Amount: \$10,707,648**
- 5% Contingency: <u>\$ 535,382</u>
- Budget:
- \$11,243,030
 - **Construction is 25% Complete**
 - Schedule: Completion June 2024
 - Budget: On Budget
 - Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Crystal Lake Park


- Prop. Bidding in July 2023
- Permits Received
- Contract Duration: Estimate 360 Days
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat

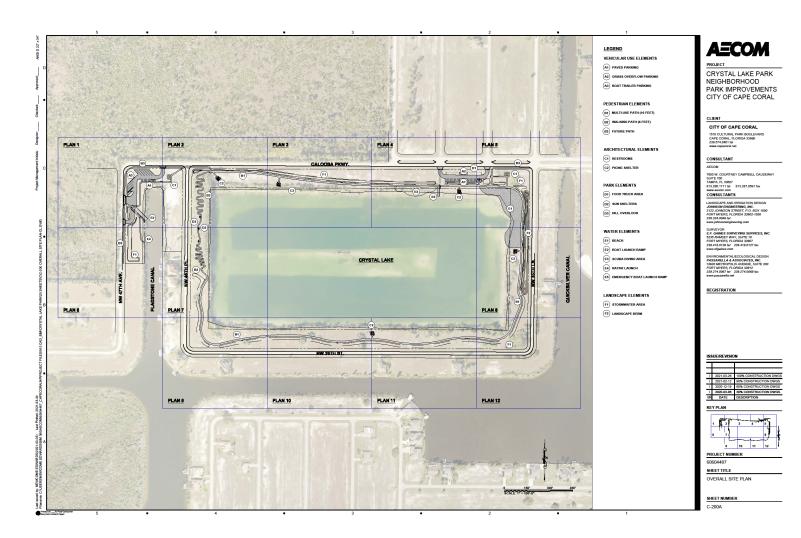



Festival Park

- Prop. Bidding in August 2023
- Base Bid 4 Fields
- Bid Add Up to 10 Fields
- Permits Received
- Contract Duration: Estimate 480 Days
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat

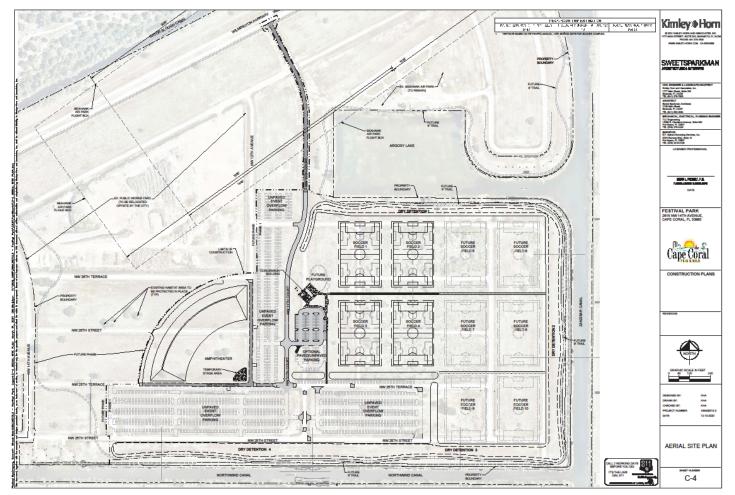




Lake Meade Park

- Prop. Bidding in August 2023
- Permits received
- Contract Duration: Estimate 420 Days
- Evaluating additional trees, sod and irrigation per discussion at the Summer


Retreat

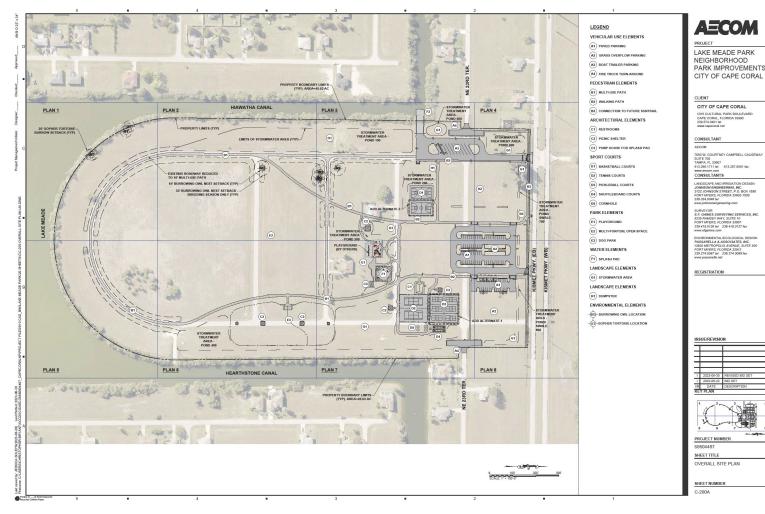



Tropicana Park

- Waiting on ACOE and SFWMD Permits
- Eagle Nest Take Permit Pending
- Contract Duration: Estimate 360 Days
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat

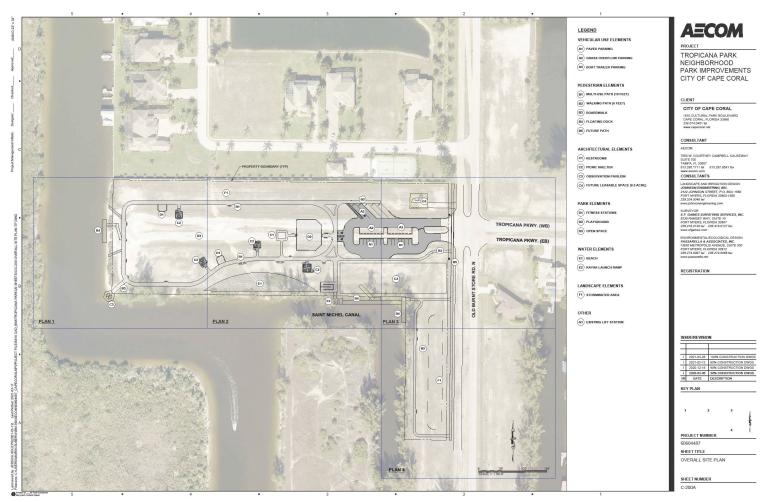



Yacht Club

- CMAR: Wright Construction
- Waiting on ACOE and DEP Permits
- GMP bidding on hold
- Boat House Opened on July 10
- Beach Opening Permits
- De-Construction and Demo KH preparing plans for bidding
- KH working on the Master Plan





Thank you

