

OFFICE OF CAPITAL IMPROVEMENTS APRIL 12, 2023



Parks GO Bond and Yacht Club

PW Coordinated the Design and Permitting & CIP Coordinating the Construction



- 1. Giuffrida Park Open
- 2. Del Prado Linear Park Open
- 3. Gator Trails Park Open
- 4. Cultural Park Open
- 5. Sands Construction 95% Complete
- 6. Coviello Construction 75% Complete
- 7. Yellow Fever Const. 20% Complete
- 8. Lake Kennedy Const. started in April
- 9. Crystal Lake Proposed Bidding in April
- 10. Festival Park Proposed Bidding in May
- 11. Lake Meade Prop. Bidding in May/June
- 12. Tropicana Permitting
- 13. Yacht Club Permitting



Giuffrida Park - Open



Contractor: EnviroStruct, LLC

Contract Amount: \$654,120

• 5% Contingency: \$ 32,706*

• Budget: \$686,826

* Contingency used for Giuffrida or Del Prado

Budget: Under Budget

Del Prado Linear Park - Open



Contractor: EnviroStruct, LLC

Contract Amount: \$1,341,221

• 5% Contingency: \$ 67,061*

• Budget: \$1,408,282

*Contingency used for Giuffrida or Del Prado

Budget: Under Budget



Gator Trails Park - Open



Contractor: Waypoint Contracting, Inc.

Original Contract Scope

• Contract Amount: \$2,114,588

• 5% Contingency: \$ 105,729*


• Budget: \$2,220,317

*Contingency used for Cultural or Gator Trails

Original Budget: Under Budget



Gator Trails Park - Open

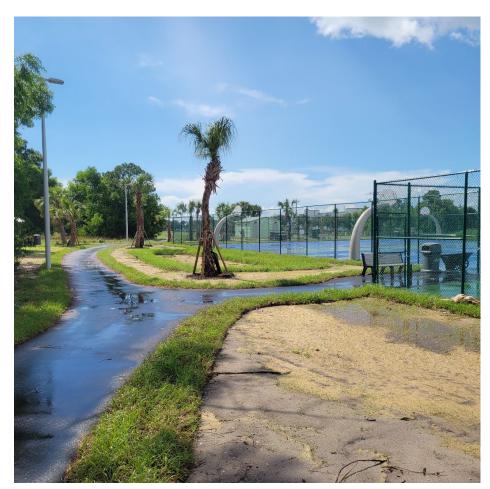

Contractor: Waypoint Contracting, Inc.

Additional Scope In Process:

- 1. Replace trees damaged by Hurricane Ian.
- 2. Add shade over existing benches.
- 3. Add shade over existing exercise equipment.



Cultural Park - Open

Original Contract Scope



• Budget: \$3,085,048

* Contingency used for Cultural or Gator Trails

- Original Schedule: Substantially Complete
- Ribbon Cutting April 21, 2023
- Original Budget: Under Budget



Contractor: Waypoint Contracting, Inc.



Cultural Park - Open



Contractor: Waypoint Contracting, Inc.

Additional Scope In Process:

- 1. Replace trees damaged by Hurricane Ian.
- 2. Add new trees and vegetation (Arbor Day Foundation Grant) Completed.
- 3. Add shade over existing benches.
- 4. Add exercise equipment with shade.
- 5. Install perimeter sidewalks Completed.
- 6. Curb and landscape 3 medians.

Sands Park



Contractor: Wright Construction

• Contract Amount: \$3,188,751

• 5% Contingency: \$ 159,438*

• Budget: \$3,348,189

*Contingency used for Sands or Joe Coviello

- Proposed Substantial Completion April 2023
- Proposed Ribbon Cutting May 2023
- Budget: On Budget

Joe Coviello Park



Contractor: Wright Construction


- Contract Amount: \$ 1,996,981
- 5% Contingency: \$ 99,849*
- Budget: \$ 2,096,830

*Contingency used for Sands or Joe Coviello

- Proposed Substantial Completion May 2023
- Proposed Ribbon Cutting June 2023
- Budget: On Budget



Yellow Fever Creek

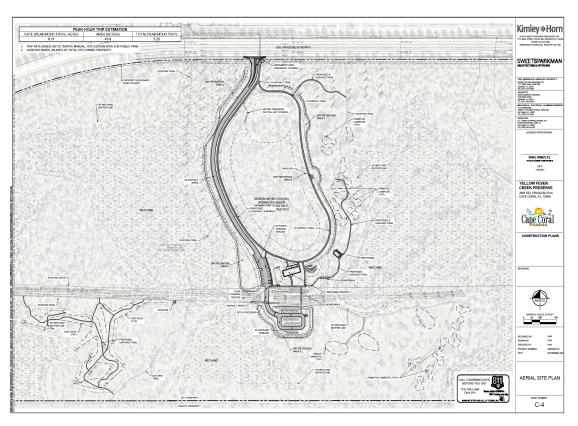

Contractor: OAC Action Construction

• Contract Amount: \$5,739,321

• 5% Contingency: <u>\$ 286,966</u>


• Budget: \$6,026,287

Schedule: Completion November 2023

Budget: On Budget



Lake Kennedy Racquet Center

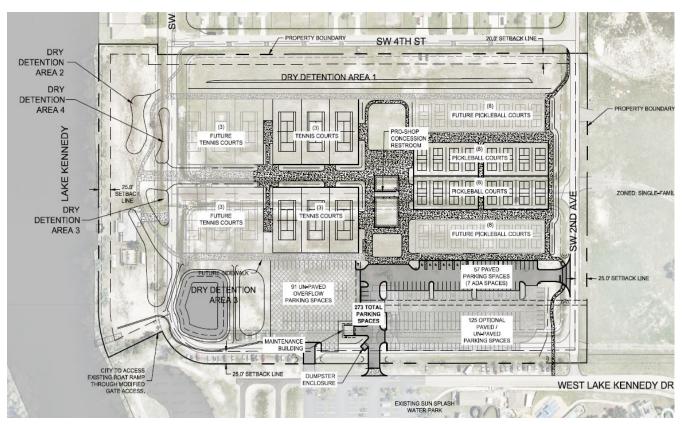

- Contract Amount: \$10,707,648
 - 5% Contingency: \$ 535,382
- Budget: \$11,243,030

- Contract Duration: 480 Days
- Schedule: Completion June 2024
- Budget: On Budget

Contractor: Charles Perry Partners, Inc.




Crystal Lake Park

 Proposed Bidding in April 2023

Permits Received


 Contract Duration: Estimate 360 Days

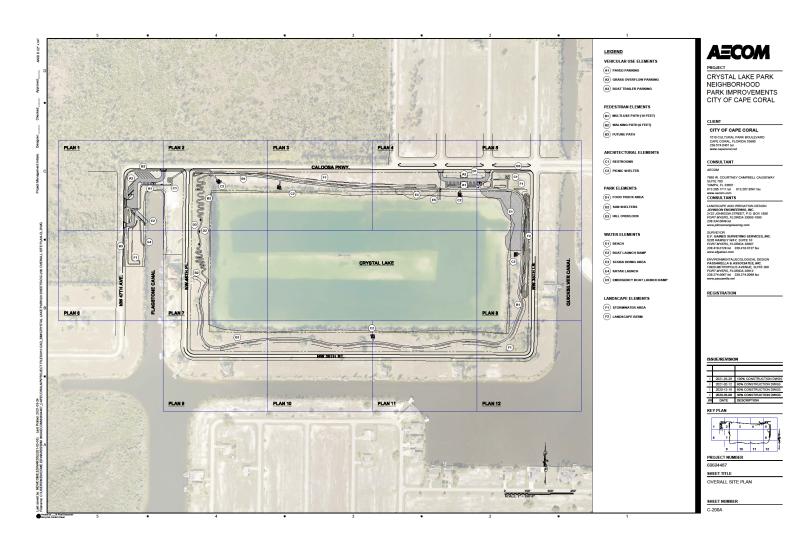



Festival Park

- Proposed Bidding in May 2023
- Permits Received
- Contract Duration:
 Estimate 480 Days

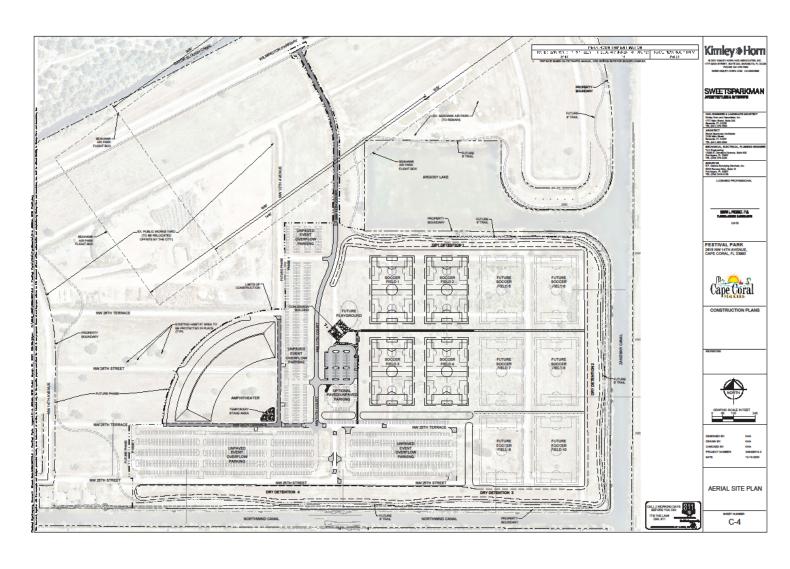




Lake Meade Park

 Proposed Bidding in May/June 2023

Permits received

 Contract Duration: Estimate 420 Days

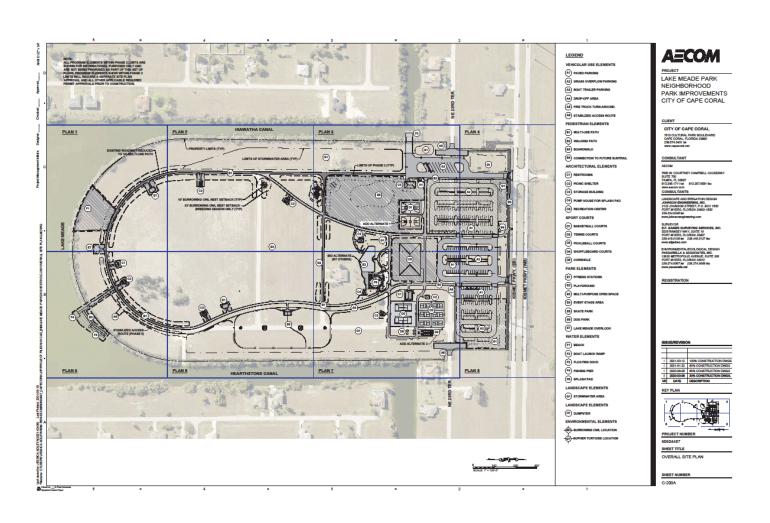




Tropicana Park

 Waiting on ACOE and SFWMD Permits

Eagle Nest Take
 Permit Pending

Contract Duration:
 Estimate 360 Days

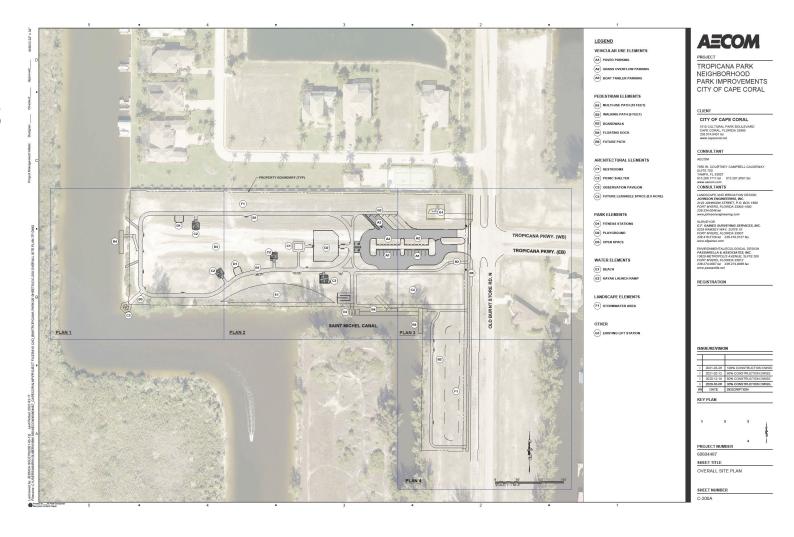



Yacht Club

- Construction Manager: Wright Construction
- Waiting on ACOE and DEP Permits
- GMP bidding on hold
- Obtaining Costs for Demolition of Existing Buildings for FEMA Reimbursement





Thank you

