

# 2023 UTILITIES PROJECTS OCTOBER 25, 2023



### I. Utilities Dept Projects

I. Ft Myers Reclaimed Water Transmission Main Const. cost \$19.7M (\$11.4M grants)

#### i. Status:

- a. Everest Pkwy Pipeline substantially complete Mar. 23'
- b. Subaqueous (HDD) section complete Jun. 23'

#### ii. Schedule:

c. Project will be completed on or before Dec. 31st

#### iii. Budget:

d. Both projects are presently under budget.

#### iv. Next Steps:

e. Conduct coordination meetings with Ft. Myers







### II. Utilities Dept Projects

II. Reservoir Pipeline and Pump Station Eng. Cost: \$822K (\$1.5M Grant)

i. Status: Recv'd 100% design Plans 3/31

ii. Schedule: On schedule


iii. Budget: On Budget

iv. Next steps:

a. Property acquisition – Dec. 23'

b. Bid project – Spring 24'

c. Project completion – Summer 25'

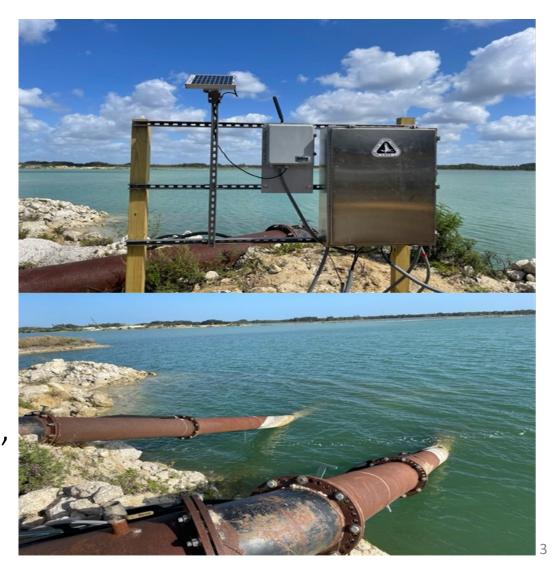



### III. Utilities Dept Projects

III. Design/permit CRA Sewer MPS-100 &FM – Est. Cost \$25M (ARPA Funded)

#### i. Forcemain Status:


- a. Construction nearing completion
- b. On Schedule and on budget

#### ii. MPS 100 Status:

- c. Project awarded to TLC
- d. Construction to begin Nov. 23'

#### iii. Next Steps:

e. Complete construction Dec. 24'

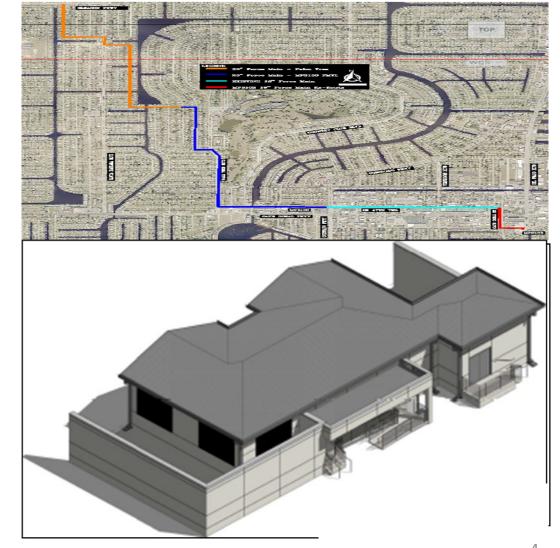




### IV. Utilities Dept Projects

IV. Palm Tree Water and FM Improvements Est. Cost \$13.1M

#### i. Status:

- a. Contract awarded Aug. 22'
- b. PO issued Sept. 22
- c. Issued Notice to Proceed Nov. 22'
- d. Complete HDD under canals Jan. 23'
- ii. Schedule: Project on schedule
- iii. Budget: Project under budget
- iv. Next steps:
  - e. Substantial Completion Nov. 23'



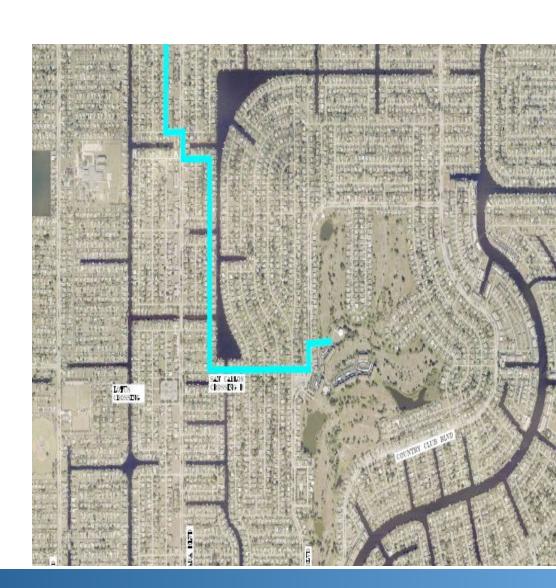

### V. Utilities Dept Projects

V. Design/permit/construct additional North RO Plant Supply Wells Estimated Cost \$10M i. Status:

- a. Eng. Contract Approved 7/11/22.
- b. Design underway.
- c. Additional well parcels acquired
- ii. Schedule: On schedule
- iii. Budget: On budget
- iv. Next steps:
  - d. Modify Water Use Permit
  - e. Complete Engineering Design
  - f. Bid Wells and Raw Water Main
  - g. Construct Wells & Raw Water Main




### VI. Utilities Dept Projects

VI. Pine Island Rd West Corridor Utilities Project. Est. Cost: \$2.4M (Engineering Design)

#### i. Status:

- a. RFP for Design Issued
- b. Engineering Consultant Selected
- c. Negotiating Contract w/Procurement
- ii. Schedule: Design schedule TBD
- iii. Budget: \$2.4M
- iv. Next Steps:
  - d. Begin Eng. Design Fall 23'
  - e. Complete Engineering Design Fall 24'

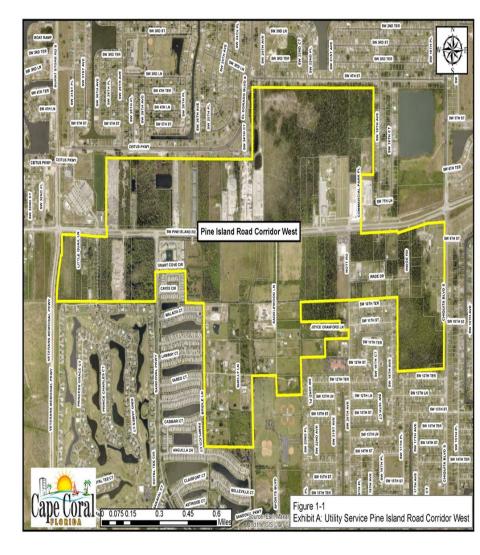



## Thank you

