





Parks GO Bond and Yacht Club Update January 18, 2023



Parks GO Bond and Yacht Club

PW Coordinating the Design and Permitting & CIP Coordinating the Construction

1.

2.

3.

4.

5.

6.

7.


8.

9.

10.

12.

13.

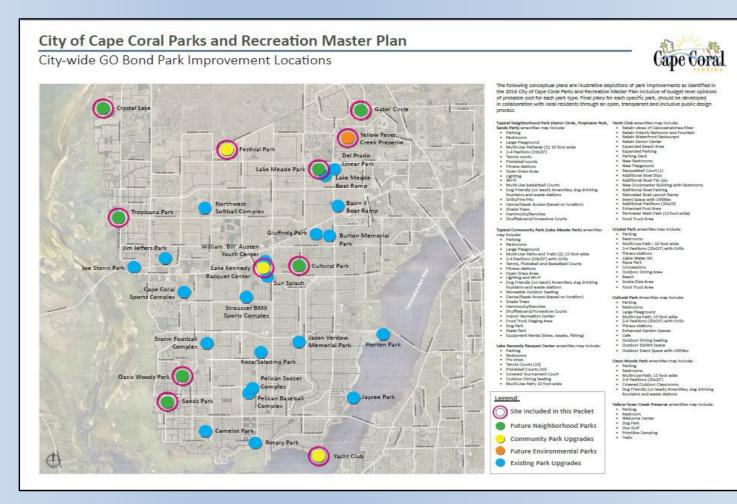

Cultural - Orig. Const. 100% Complete Gator - Orig. Const. 100% Complete **Giuffrida - Construction 100% Complete Del Prado - Construction 95% Complete Sands - Construction 95% Complete Coviello - Construction 60% Complete Yellow Fever - Construction 10% Complete** Lake Kennedy - NTP in March 2023 Festival Park - Proposed Bidding Feb. 2023 Lake Mead - Proposed Bidding March 2023 **Crystal Lake - Proposed Bidding March 2023 Tropicana - Permitting Yacht Club - Permitting**



Cultural Park



Original Contract Scope

 Contract Amount: \$2,938,141

 5% Contingency:
 \$146,907*

 Budget:
 \$3,085,048

* Contingency can be used for Cultural or Gator Trails Parks

Original Schedule: Substantially Complete

Original Budget: Under Budget

Contractor: Waypoint Contracting, Inc.



Cultural Park



Additional Scope Proposed:

- **1. Replace trees damaged by Hurricane lan**
- 2. Add new trees and vegetation
- 3. Add shade over existing benches
- 4. Add exercise equipment with shade
- 5. Install perimeter sidewalks
- 6. Curb and landscape 3 medians

Staff presently obtaining costs.



Gator Trails Park



Original Contract Scope

Contract Amount: \$2,114,588						
5% Contingency:	<u>\$105,729*</u>					
Budget:	\$2,220,317					

* Contingency can be used for Cultural or Gator Trails Parks

Original Schedule: Substantially Complete

Original Budget: Under Budget

Contractor: Waypoint Contracting, Inc.



Gator Trails Park



Additional Scope Proposed:

- **1. Replace trees damaged by Hurricane Ian**
- 2. Add new trees and vegetation
- 3. Add shade over existing benches
- 4. Add shade over exist. exercise equipment

Staff presently obtaining costs.



Giuffrida Park



 Contract Amount:
 \$654,120

 5% Contingency:
 \$32,706*

 Budget:
 \$686,826

* Contingency can be used for Giuffrida or Del Prado Parks

Schedule: Project Complete

Budget: Under Budget

Contractor: Enviro Struct, LLC



Del Prado Linear Park



Contractor: Enviro Struct, LLC

 Contract Amount:
 \$1,341,221

 5% Contingency:
 \$67,061*

 Budget:
 \$1,408,282

* Contingency can be used for Giuffrida or Del Prado Parks

Schedule: 5 Month Time Extension Due to Supply Chain Issues, LCEC, and Hurricane Ian. Proposed Substantial Completion Feb. 2023

Budget: Under Budget



Sands Park



Contractor: Wright Construction

 Contract Amount:
 \$3,188,751

 5% Contingency:
 \$159,438*

 Budget:
 \$3,348,189

* Contingency can be used for Sands or Joe Coviello Parks

Schedule: 3 Month Time Extension Due to Supply Chain Issues, LCEC, and Hurricane Ian. Proposed Substantial Completion Jan/Feb. 2023

Budget: On Budget



Joe Coviello Park



Contractor: Wright Construction

 Contract Amount:
 \$1,996,981

 5% Contingency:
 \$99,849*

 Budget:
 \$2,096,830


* Contingency can be used for Sands or Joe Coviello Parks

Schedule: 5 Month Time Extension Due to Supply Chain Issues, LCEC, and Hurricane Ian. Proposed Substantial Completion March 2023

Budget: On Budget



Yellow Fever Creek

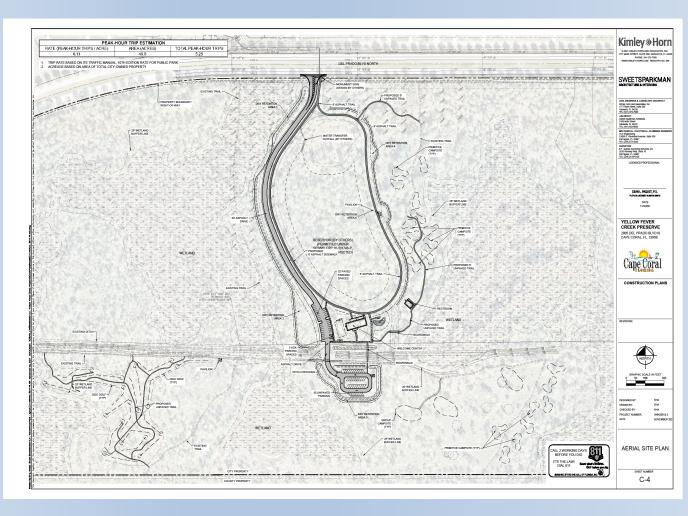

 Contract Amount:
 \$5,739,321

 5% Contingency:
 \$286,966

 Budget:
 \$6,026,287

Schedule:


Completion August 2023

Budget: On Budget

Contractor: OAC Action Construction



Lake Kennedy Racquet Center

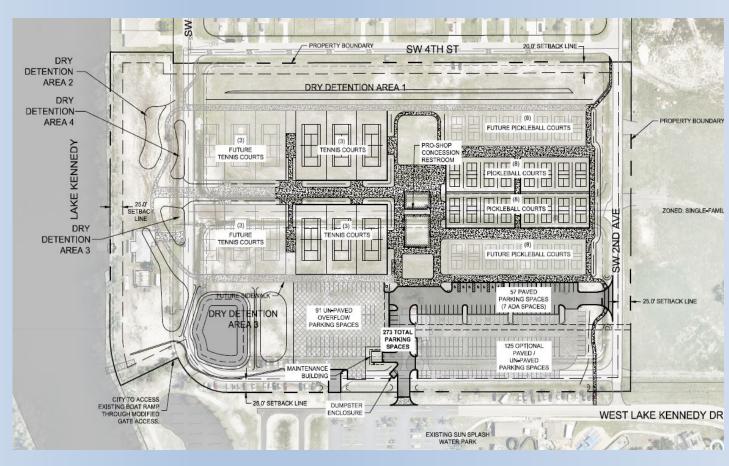

 Contract Amount:
 \$10,707,648

 5% Contingency:
 \$535,382

 Budget:
 \$11,243,030


Contract Duration: 480 DaysSchedule: NTP in March 2023Budget: On Budget

Contractor: Charles Perry Partners, Inc.



Festival Park


- Proposed Bidding in Feb 2023
- Permits Received
- Contract Duration: Estimate 480 Days

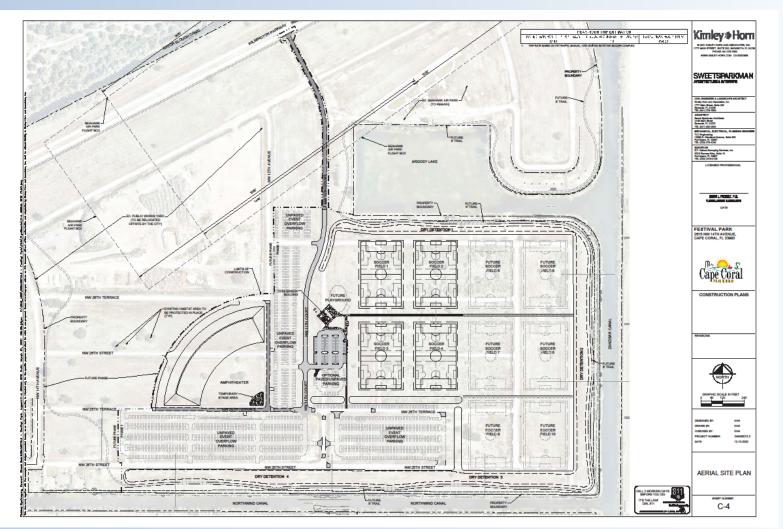



Lake Meade Park


- Proposed Bidding in March 2023
- Permits received
- Contract Duration: Estimate 420 Days

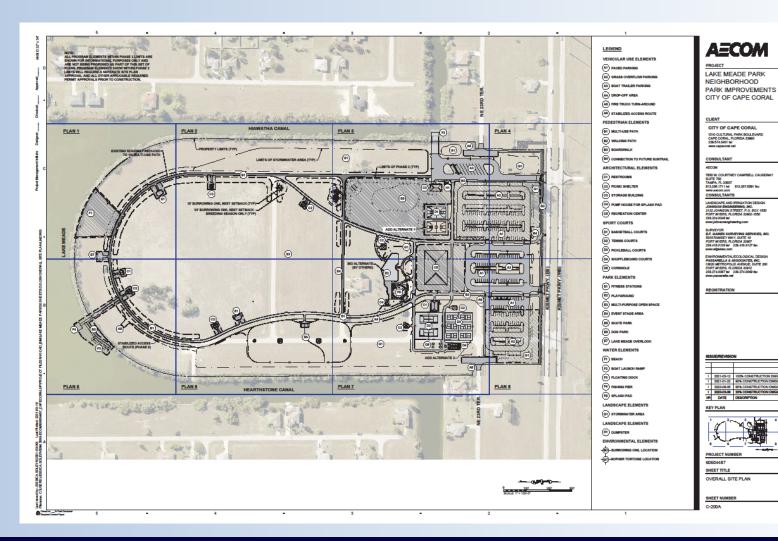



Crystal Lake Park


- Proposed Bidding in March 2023
- Permits Received
- Contract Duration: Estimate 360 Days

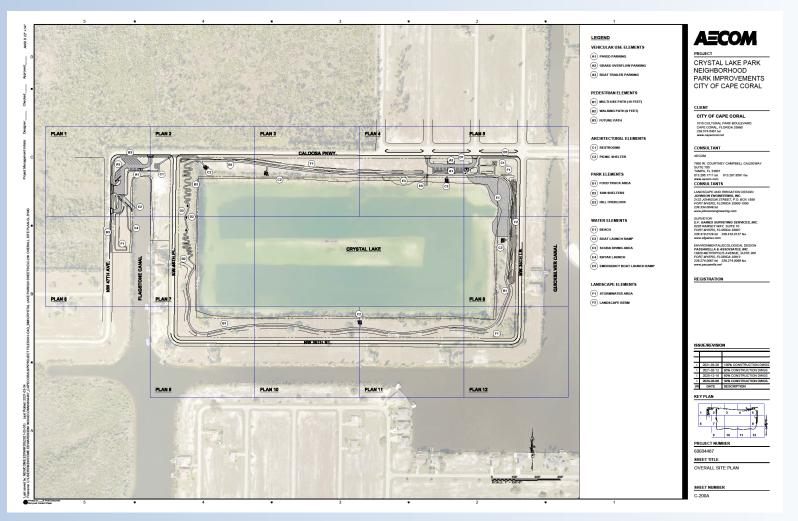



Tropicana Park

- Waiting on ACOE and SFWMD Permits
- Contract Duration: Estimate 360 Days

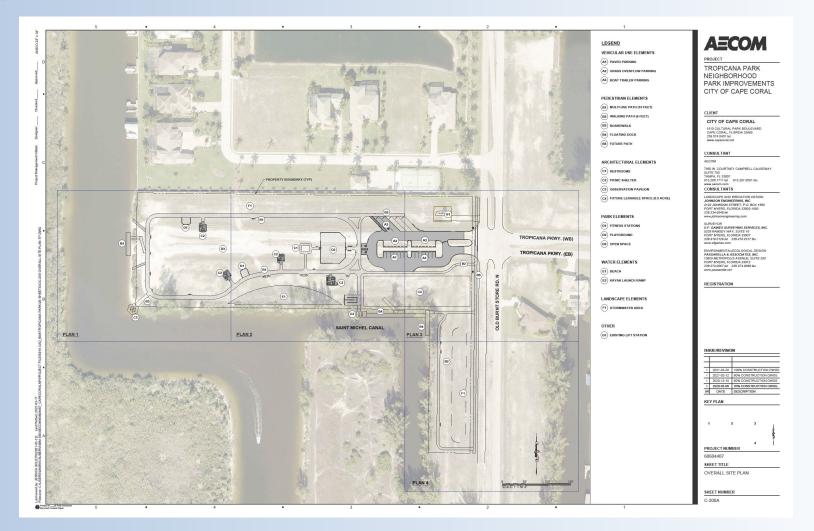



Yacht Club

- Construction Manager: Wright Construction
- Waiting on ACOE and DEP Permits
- GMP bidding on hold
- Detailed Discussions at the Jan 2023 Winter Retreat





	Parks GO Bond									
	Summary of Estimated Costs									
Status	GO Bond Initial Estimates (2018)	Parks	Actual or Current Estimates	1/17/202 Contingency	Actual or Current Total Estimates	Current Remaining Contingency	Other Funds	Comments		
	\$510,000	Sun Shades	\$1,123,177	\$112,318	\$1,235,495	\$222,154				
	\$4,513,340	Cultural	\$2,938,141	J112,510	Ş1,233,433	<i>7222,</i> 134				
	\$2,572,444	Gator	\$2,114,588	\$252,636	\$5,305,366	\$40,454		Substantially Complete		
	\$0	Cultural and Gator			\$650,000			Proposed Additional Scope		
	\$470,000	Giuffrida	\$654,120							
	\$1,000,000	Del Prado	\$1,341,221	\$99,767	\$2,095,108	\$41,774		Giuffrida Complete		
Parks Bid	\$3,675,424	Sands	\$3,188,751							
	\$2,426,479	Coviello	\$1,996,981	\$259,287	\$5,696,809	\$170,368				
	\$0	Amend #1 - Exotics	\$251,790							
	\$3,900,000	Yellow Fever Creek	\$5,739,321	\$286,966	\$6,026,287	\$286,966				
	\$4,994,499	Lake Kennedy	\$10,707,648	\$535,382	\$11,243,031	\$535,383				
	\$24,062,186	Sub Totals	\$30,055,738	\$1,546,356	\$32,252,095	\$1,297,098				
r I				Г						
Parks To	\$5,882,500	Festival Park	\$9,724,664	\$486,233	\$10,210,898			Includes 20% Cost Escalation and \$500,000 Bid Additive		
	\$6,589,916	Lake Meade	\$9,013,600	\$450,680	\$9,464,280			Includes 20% Cost Escalation and \$500,000 Bid Additive		
Be Bid	\$3,185,748	Crystal Lake	\$5,445,348	\$272,267	\$5,717,615			Includes 20% Cost Escalation		
	\$2,928,778	Tropicana	\$4,017,814	\$200,891	\$4,218,704			Includes 20% Cost Escalation		
	\$18,586,942	Sub Totals	\$28,201,426	\$1,410,071	<mark>\$29,611,497</mark>					
 _	\$185,000	BMX			\$65,160			Complete		
-	\$185,000	Burton			\$03,100			Included in Sun Shades Contract		
-	\$262,000	Horton			\$94,500			Complete		
	\$260,000	Jason Verdow			\$260,000			Lighting Project Underway		
	\$300,000	Koza Saldina			\$307,478			Complete		
Misc.	\$550,000	Northwest Softball			\$377,427			Complete		
Parks	\$200,000 \$500,000	Parks Wi-Fi Pelican Baseball			\$200,000 \$299,899			Complete		
	\$100,000	Pelican Soccer			\$299,899 \$99,014			Complete		
	\$235,000	Storm Football			\$148,193			Complete		
	\$2,777,000	Sub Totals	\$0	\$0	\$1,851,671					
<u>г</u>	\$1,900,000	Multi Sports Land			\$1,503,666			Land Purchase		
	\$10,980,027	Yacht Club						Not included in GO Bond		
	\$1,846,364	Construction Contingency								
		City Project Management			\$745,139					
		AIM			\$185,303		6202.000			
Misc.		AECOM AECOM Additional			\$3,079,384 \$100,000		\$303,999	D&D Design		
∥ ⊦		Kimley Horn GO			\$1,962,940					
		Kimley Horn Yacht Club			\$2,174,412			Yacht Club Design		
		Wright (CMAR)			\$331,287			Yacht Club CMAR Phase 1		
	\$14,726,391	Sub Totals	\$0	\$0	<mark>\$10,082,131</mark>					
TOTALS	\$60 1F2 F10				\$73,797,393					
IJIALS	\$60,152,519				225,121,223					

Original GO Bond	\$60,152,519		
Parks GF Restricted Reserves Available	\$12,842,921		
Total Available	\$72,995,440		
