


OFFICE OF CAPITAL IMPROVEMENTS OCTOBER 25, 2023



Parks GO Bond and Yacht Club

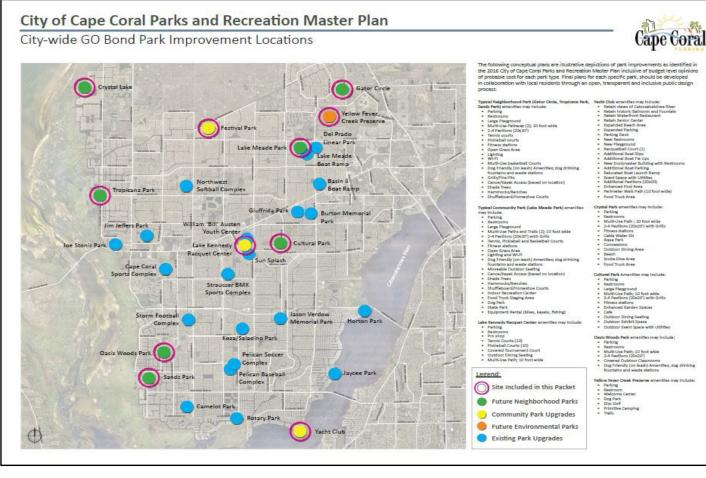

- 1. Giuffrida Park Open
- 2. Del Prado Linear Park Open
- 3. Gator Trails Park Open Add. Scope
- 4. Cultural Park Open Add. Scope
- 5. Sands Soft Opening Add. Scope
- 6. Coviello Soft Opening Add. Scope
- 7. Yellow Fever Const. 50% Complete
- 8. Lake Kennedy Const. 35% Complete
- 9. Crystal Lake Bids received in Sept.
- 10. Festival Park Bid Opening Nov. 15
- 11. Lake Meade Prop. Bidding in Dec.
- 12. Tropicana Permitting
- 13. Yacht Club Permitting



Gator Trails Park - Open



Contractor: Waypoint Contracting, Inc.

(No Further Updates)

Original Contract Scope

Contract Amount: \$2,114,588

• 5% Contingency: \$ 105,729*

• Budget: \$2,220,317

*Contingency used for Cultural or Gator Trails

 Original Schedule: Substantially Complete





Gator Trails Park - Open



Contractor: Waypoint Contracting, Inc.

(No Further Updates)

Additional Scope In Process:

- Replacing trees and irrigation damaged by Hurricane Ian in October.
- 2. Add shade over existing benches In Process.
- 3. Add shade over existing exercise equipment In Process.
- Evaluated additional trees, sod and irrigation per discussion at the Summer Retreat - None required.

Cultural Park - Open

Cultural Park has been chosen to be included in the 2023 Florida Recreation & Parks Association Annual Showcase



Contractor: Waypoint Contracting, Inc.

Original Contract Scope

Contract Amount: \$2,938,141

• 5% Contingency: \$ 146,907*

• Budget: \$3,085,048

* Contingency used for Cultural or Gator Trails

 Original Schedule: Substantially Complete



Cultural Park - Open



Additional Scope In Process:

- 1. Install perimeter sidewalks Completed
- 2. Added 60 new trees and vegetation (Arbor Day Foundation Grant)-Completed
- 3. Replace trees and irrigation damaged by Hurricane Ian. Adding 30 trees In Oct. and Nov.
- Add shade over existing benches -In Process.
- 5. Curb 3 medians Completed
- 6. Landscape 3 medians In Process
- 7. Evaluated additional trees, sod and irrigation per discussion at the Summer Retreat Additional trees to be added through future grants



Contractor: Waypoint Contracting, Inc.

Sands Park - Soft Opening



Contract Amount: \$3,188,751

• 5% Contingency: \$ 159,438*

• Budget: \$3,348,189

*Contingency used for Sands or Coviello

 Substantial Completion in April 2023

Ribbon Cutting in November

Contractor: Wright Construction

- Evaluated additional trees, sod and irrigation per discussion at the Summer Retreat – In Process
 - Adding Palm Trees w/irrigation and sod at entrance.
 - Adding Cypress Trees w/irrigation at detention areas.



Joe Coviello Park - Soft Opening



Contract Amount: \$1,996,981

• 5% Contingency: \$ 99,849*

Budget: \$2,096,830

*Contingency used for Sands or Coviello Parks

- Substantial Completion in August 2023
- Ribbon Cutting in November
- Evaluated additional trees, sod and irrigation per discussion at the Summer Retreat In Process
 - Adding Sod at the Park Entrance





Yellow Fever Creek



- Contract Amount: \$5,739,321
- 5% Contingency: <u>\$ 286,966</u>
- Budget: \$6,026,287
- Construction is 50% complete
- Schedule: Completion Feb 2024
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat - None Required



Contractor: OAC Action Construction

Lake Kennedy Racquet Center




- Contract Amount: \$10,707,648
- 5% Contingency: \$ 535,382
- Budget: \$11,243,030
- Construction is 35% Complete
- No. The state of t
- Schedule: Completion June 2024
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Contractor: Charles Perry Partners, Inc.

Crystal Lake Park

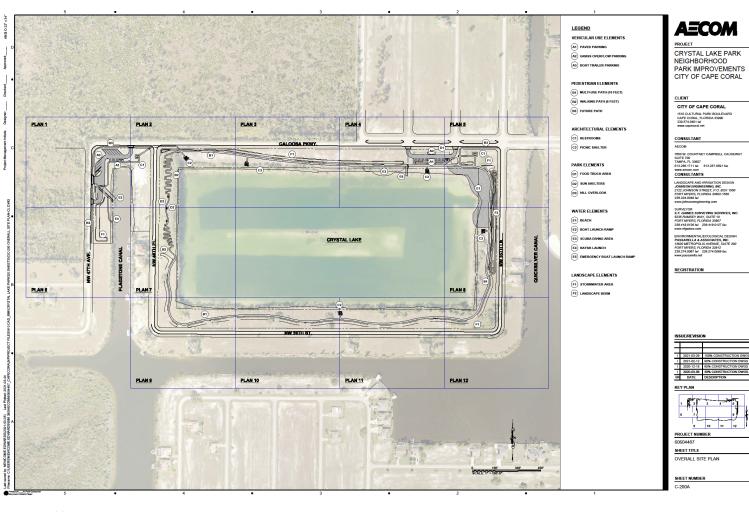


- One Bid submitted in September 2023
- Base Bid = \$9,063,714
 Bid Adds = \$1,229,433
 \$10,293,147
- CIP and Procurement reviewing the Contractor's Qualifications and their Bid
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat




Festival Park

- Bid Opening November 15, 2023
- Base Bid 4 Fields
 Bid Add Up to total of 10 Fields
- Contract Duration: Estimate 480 Days
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat

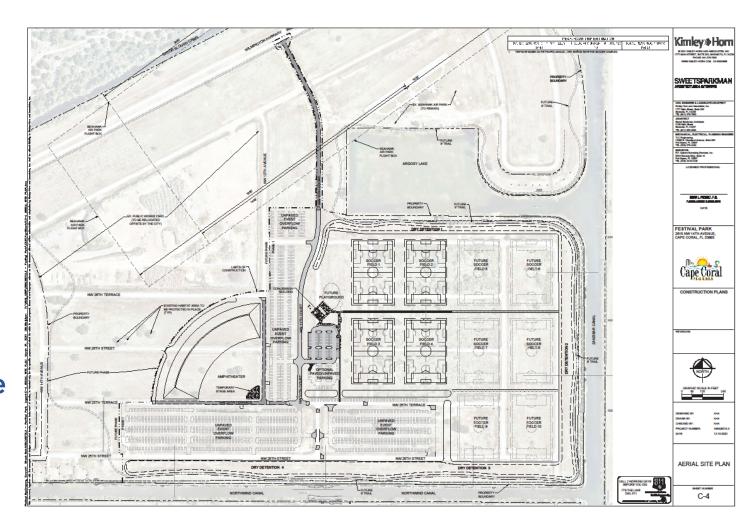



Lake Meade Park

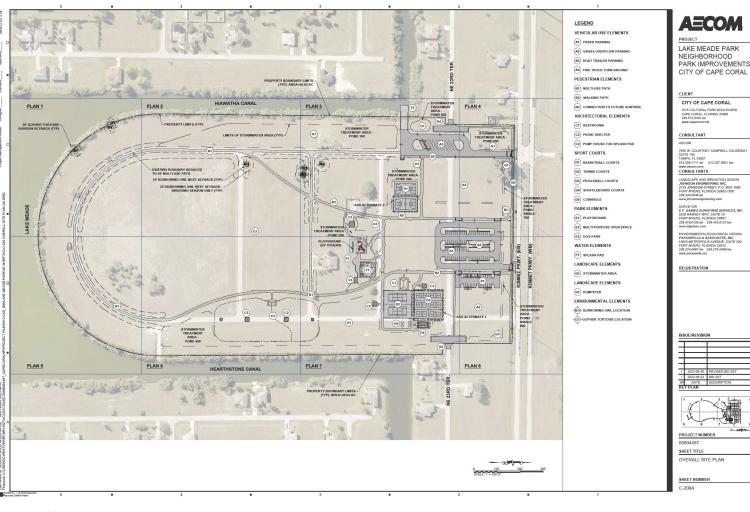


 Possible P3 for Community Center, Pool, Indoor Recreation, Etc.

- Permits Received
- Proposed Bidding in Dec.
- Contract Duration: Estimate 420 Days
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Tropicana Park

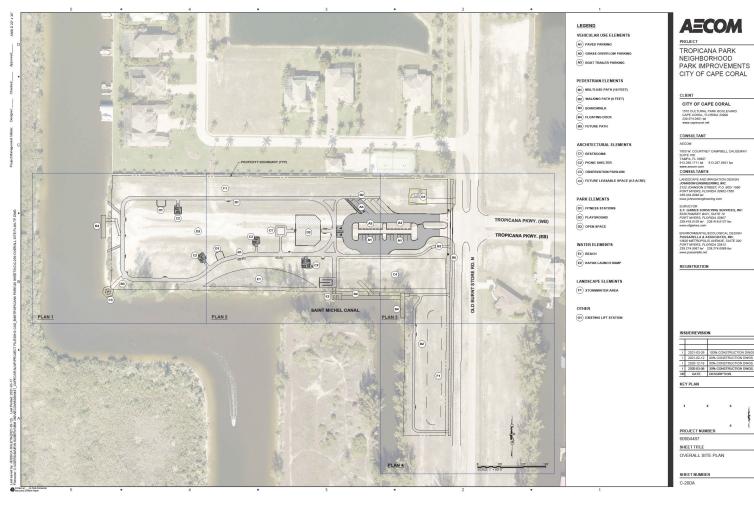

- Waiting on USACE Permit
- Obtained SFWMD Permit
- Exotic Tree Removal and Eagle Nest Take Completed
- Contract Duration: Estimate 360 Days
- Evaluating additional trees, sod and irrigation per discussion at the Summer Retreat



Yacht Club

- Design: Kimley-Horn (KH)
- CMAR: Wright Construction
- Waiting on USACE and FDEP Permits
- GMP bidding on hold
- Beach Opening USACE Permits
- De-Construction and Demo KH preparing plans for bidding
- Master Plan Discussion at the Nov 8 COW





Thank you

